


Ryan Corner Wind Farm

Weekly Construction Report March 20, 2023

General:

Weather continues to be pleasant, and work can continue to progress across the site. The Vestas site offices have been delivered, concreting around their compound is underway and the services will be connected ready for the staff to move in. The GPS installed in the earthmoving plant shows the layout of the access tracks and any “no go zones”. This is needed in the event that the barriers are damaged by stock or other incidents

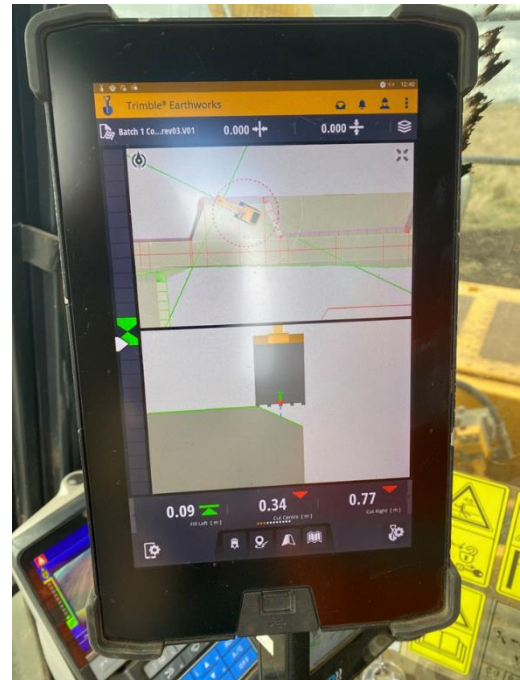

Foundations:

Work has commenced on 34 foundations and 17 of these have had the final concrete pour. Batch 1 (the western side of Riverside Road) has had all access tracks and foundations excavated: 12 of the 17 turbines in batch 1 poured. This will be the first section to be handed to Vestas for turbine erection. A crusher bucket on an excavator is being trialed, so far it is proving successful.

Connections:

RJE trenching for internal cables have 3 crews excavating and installing cables. The picture to the right shows the trencher moving alongside the access track. The foundations on the northern end of the transmission line have to be drilled and concrete poured.



Ryan Corner Development Pty. Ltd.

Phone: 0428 867 646 (Debra Dumesny – Community and Stakeholder Engagement)

Email: ryancornerwindfarm@globalpower-generation.com.au or debra.dumesny@globalpower-generation.com.au

Website: www.ryancornerwindfarm.com.au

Mail: Ryan Corner Development Pty Ltd, Suite A, Level 3, 73 Northbourne Avenue, Canberra ACT 2601
